US Army Corps of Engineers

2005 Hurricane Season Region/ Division Perspectives

FEMA

- Region IV
- Region VI
- SAD
- MVD
- SWD

US Army Corps of Engineers

USACE/FEMA 2005/2006 Hurricane Season Critique and Planning Workshop
March 07– March 09 2006
Arlington, TX

FEMA

FEMA Region VI Perspective

US Army Corps of Engineers

Katrina Timeline for Louisiana

FEMA

- 08/27: Region VI RRCC activated in Denton at Level 1
- 08/27: LA EOC activated at Level 1; ERT A deployed
- 08/27: President declares FEMA-3212-EM-LA
- 08/29: Hurricane Katrina made landfall in southeastern

  Louisiana as a Category four (4) hurricane
- 08/29: President declares FEMA-1603-DR-LA
- 09/02: President declares FEMA-3215-EM-AR
- 09/05: President declares FEMA-3219-EM-OK
- 09/07: President declares FEMA-3229-EM-NM
- 09/12: JFO becomes fully operational in LA

Wind Speed and Storm Surge

FEMA

Hurricane Katrina

FEMA-1603-DR-LA
FEMA-1607-DR-LA

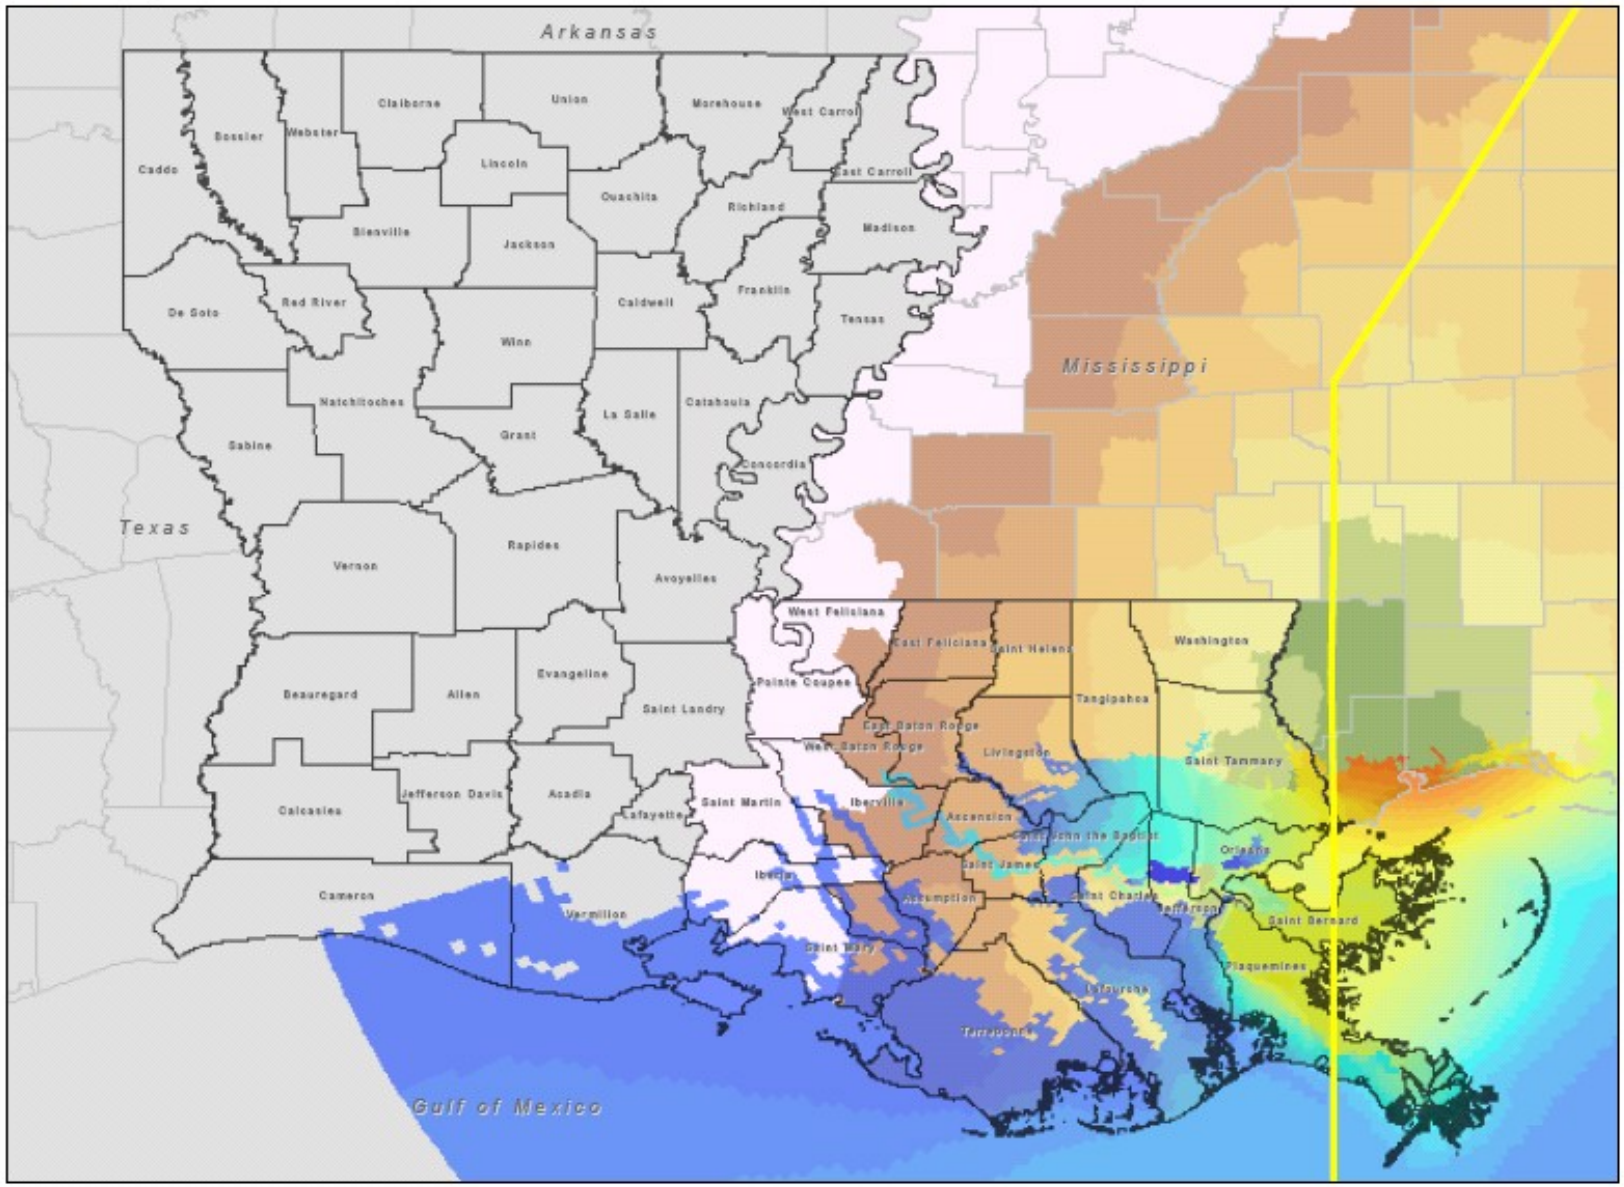

urricane Katrina Predicted Rainfall Totals by Coun
August 29 – September 01, 2005

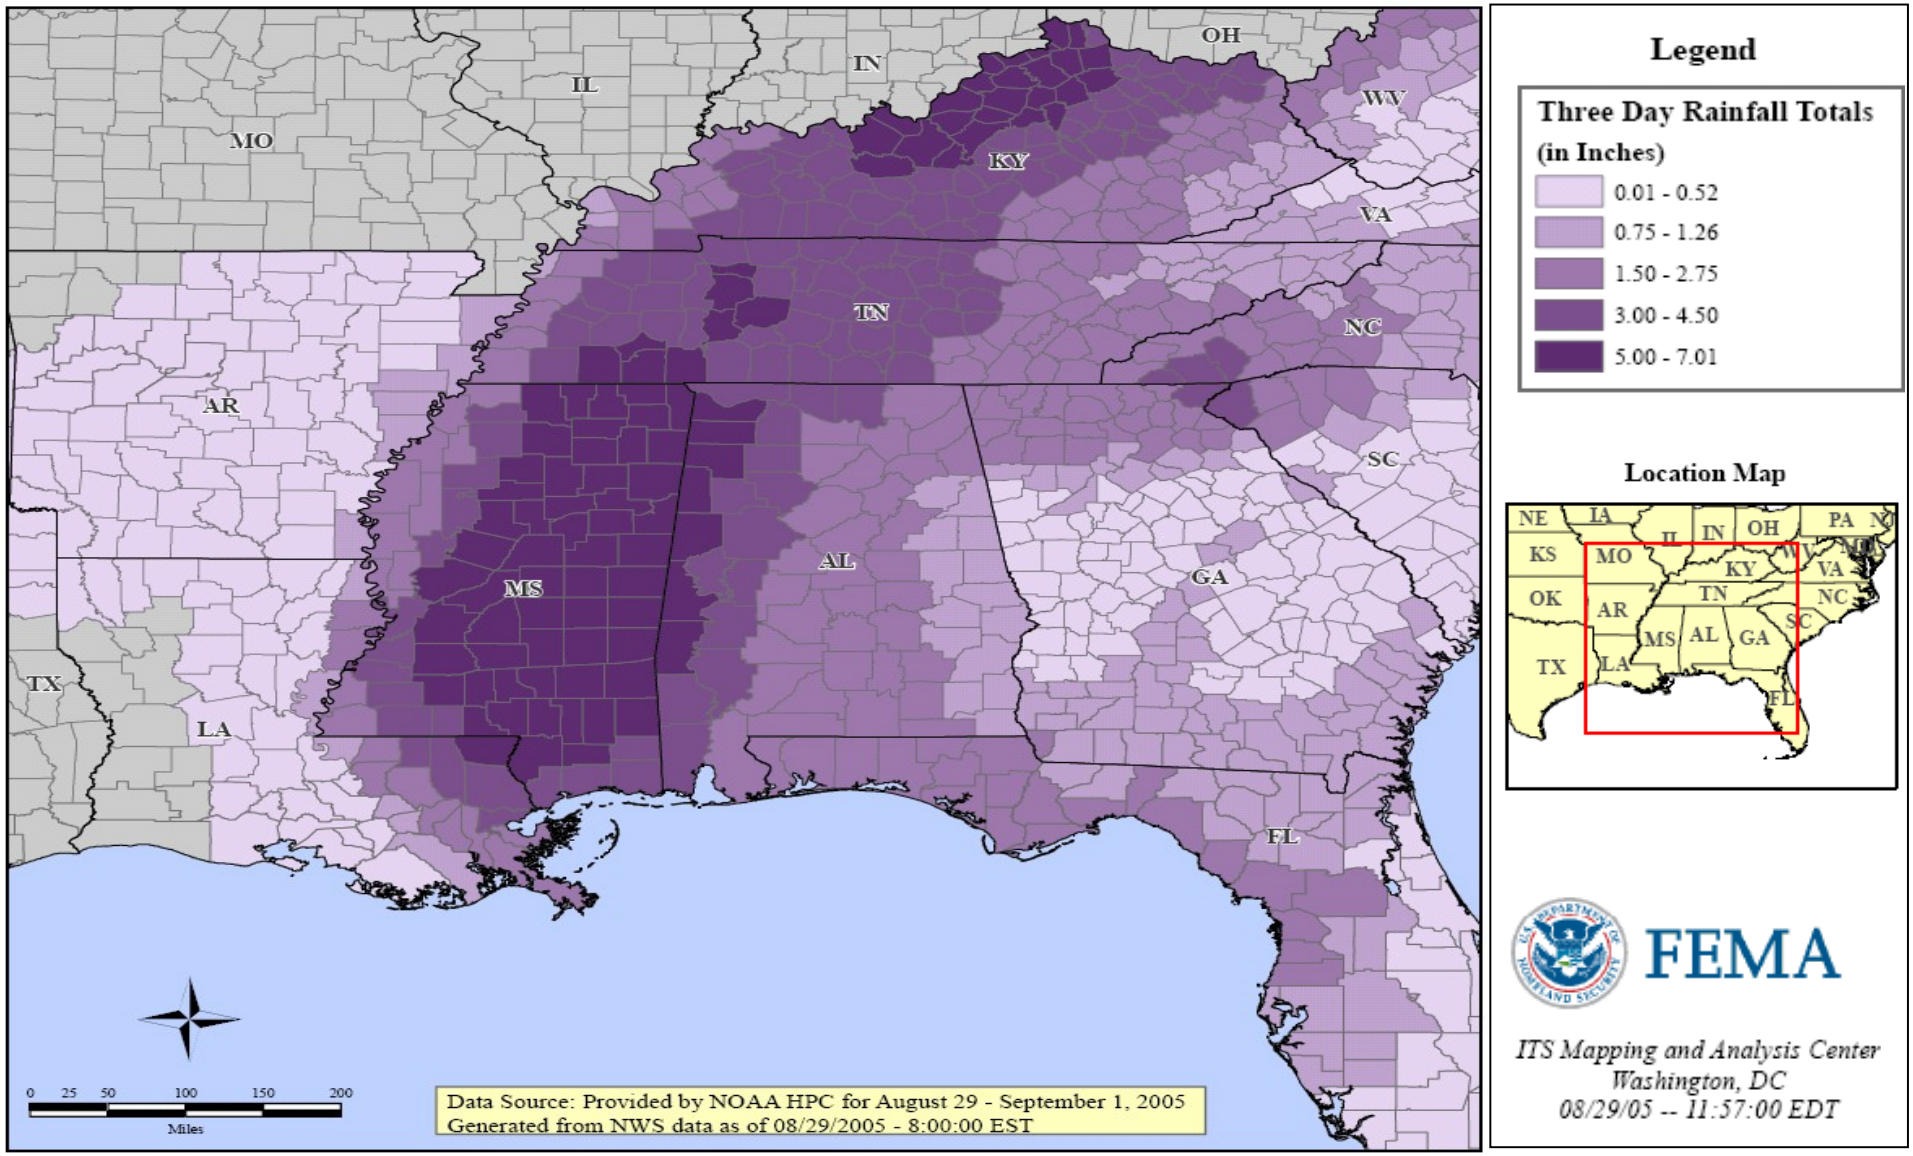

Legend

Three Day Rainfall Totals (in Inches)

- 0.01 - 0.52
- 0.75 - 1.26
- 1.50 - 2.75
- 3.00 - 4.50
- 5.00 - 7.01

Location Map

FEMA

ITS Mapping and Analysis Center
Washington, DC
08/29/05 -- 11:57:00 EDT

US Army Corps of Engineers

Rita Timeline for Louisiana

FEMA

- 09/21: President declares FEMA-3260-EM-LA
- 09/24: President declares FEMA-1607-DR-LA
- 09/24: At 0230 CDT Hurricane Rita makes landfall near Sabine Pass, Texas as a Category three (3)

US Army Corps of Engineers

Louisiana Commodities for Katrina and Rita

FEMA

- Ice
  - 2,120 Truck loads delivered (89M lbs)
- Water
  - 2,310 Truck loads delivered (10.4M lbs)
- Power
  - Approx. 330 generators used

US Army Corps of Engineers

Temporary Roofing Operation Blue Roof for Louisiana

FEMA

Katrina and Rita:

- 80,469 roofs installed
- 36 parishes included in Blue Roof Operation

Temporary Roofing Status as of 22 February 2006

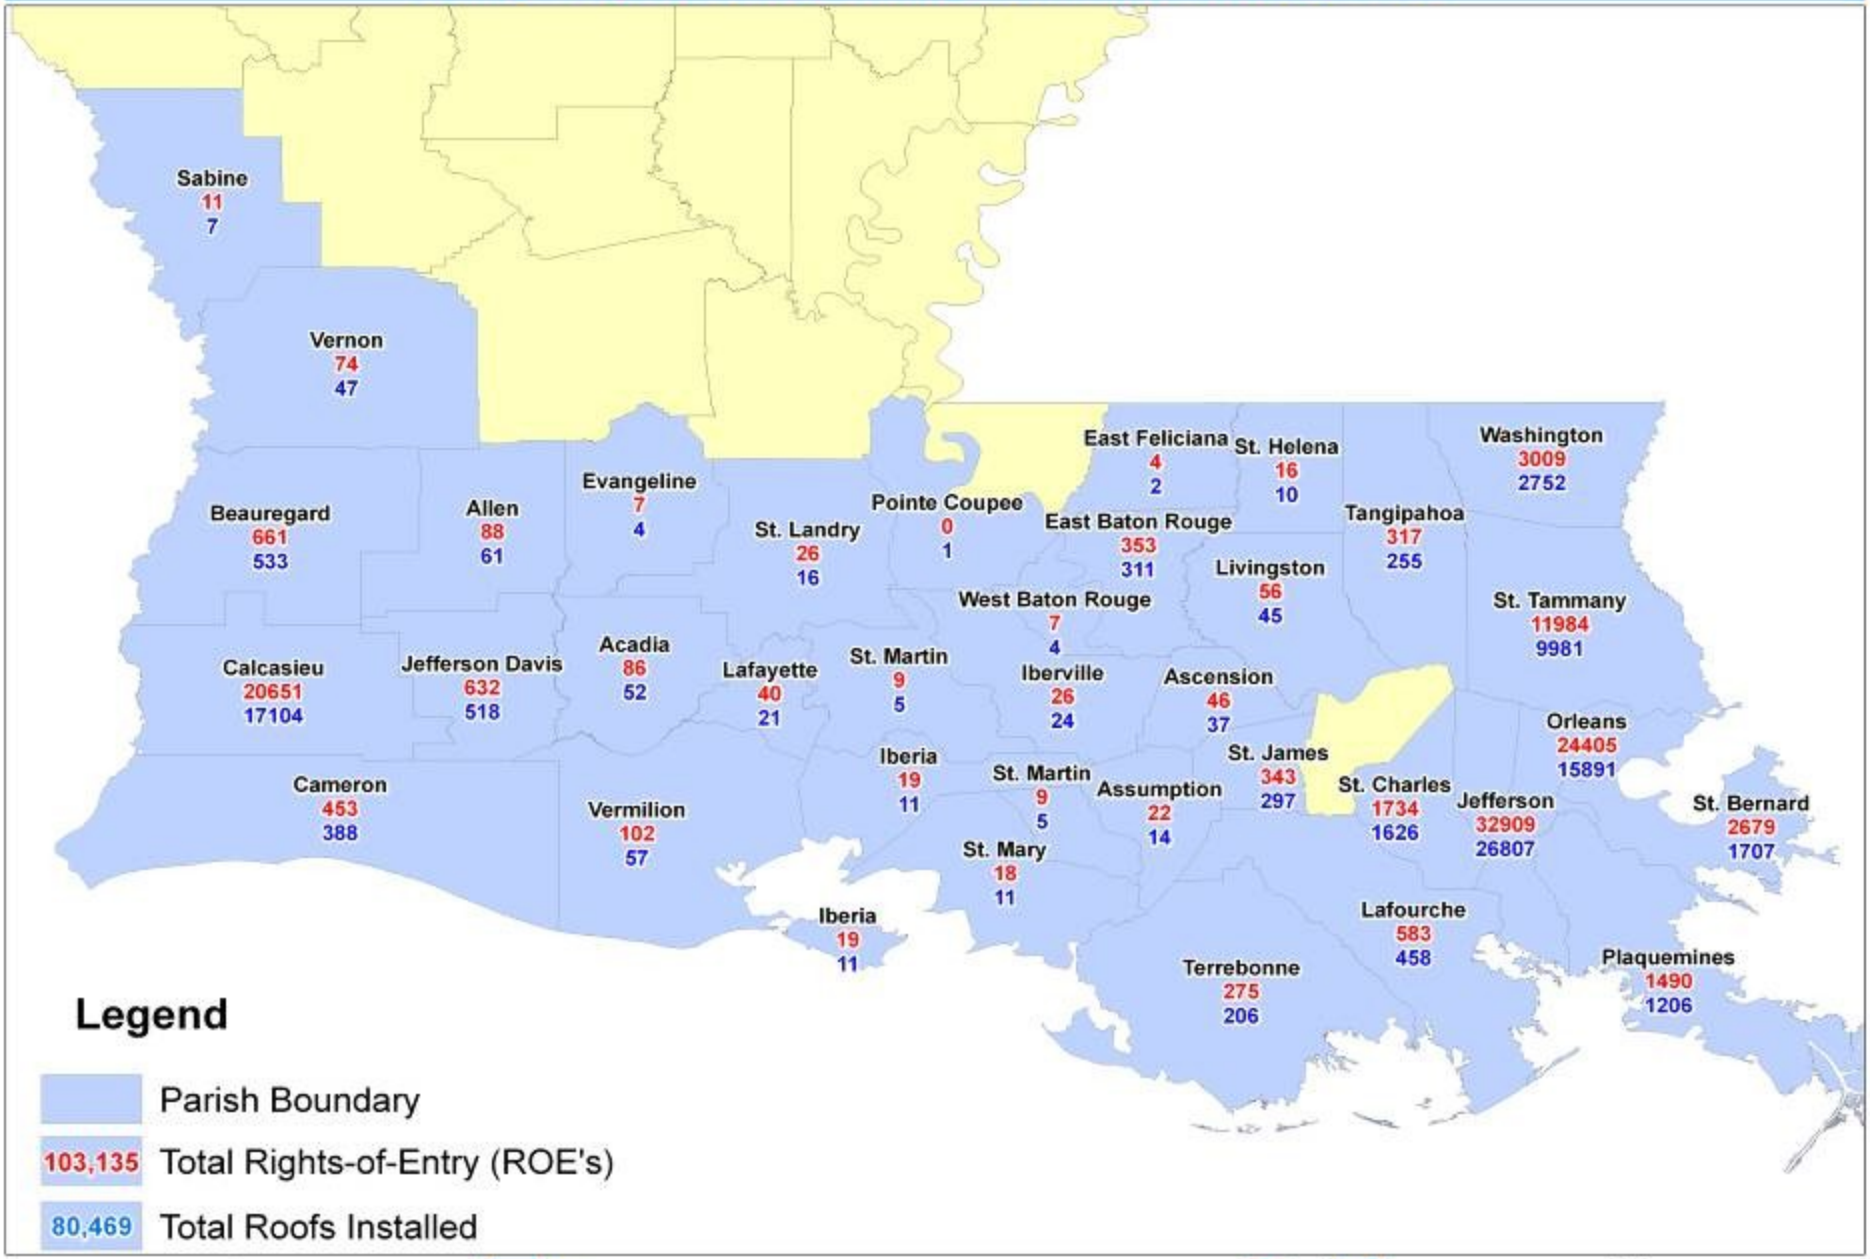

Legend

Parish Boundary

103,135 Total Rights-of-Entry (ROE's)

80,469 Total Roofs Installed

FEMA

ID: FEMA-3216_DR-LA
Blue_Roof_Status_20060202.mxd
GIS:EMAAK

US Army Corps of Engineers

Miles
10 5 0 10 20 30 40 50 60 70

US Army Corps of Engineers

Debris Removal for Louisiana

FEMA

- 63 million CY total estimated
- 35.2 million CY removed / 56% complete
- White Goods:
  - 321,000 units collected
- Hazardous Waste
  - 14 million lbs. collected

Applicant and USACE Managed Debris FEMA-1603-1607

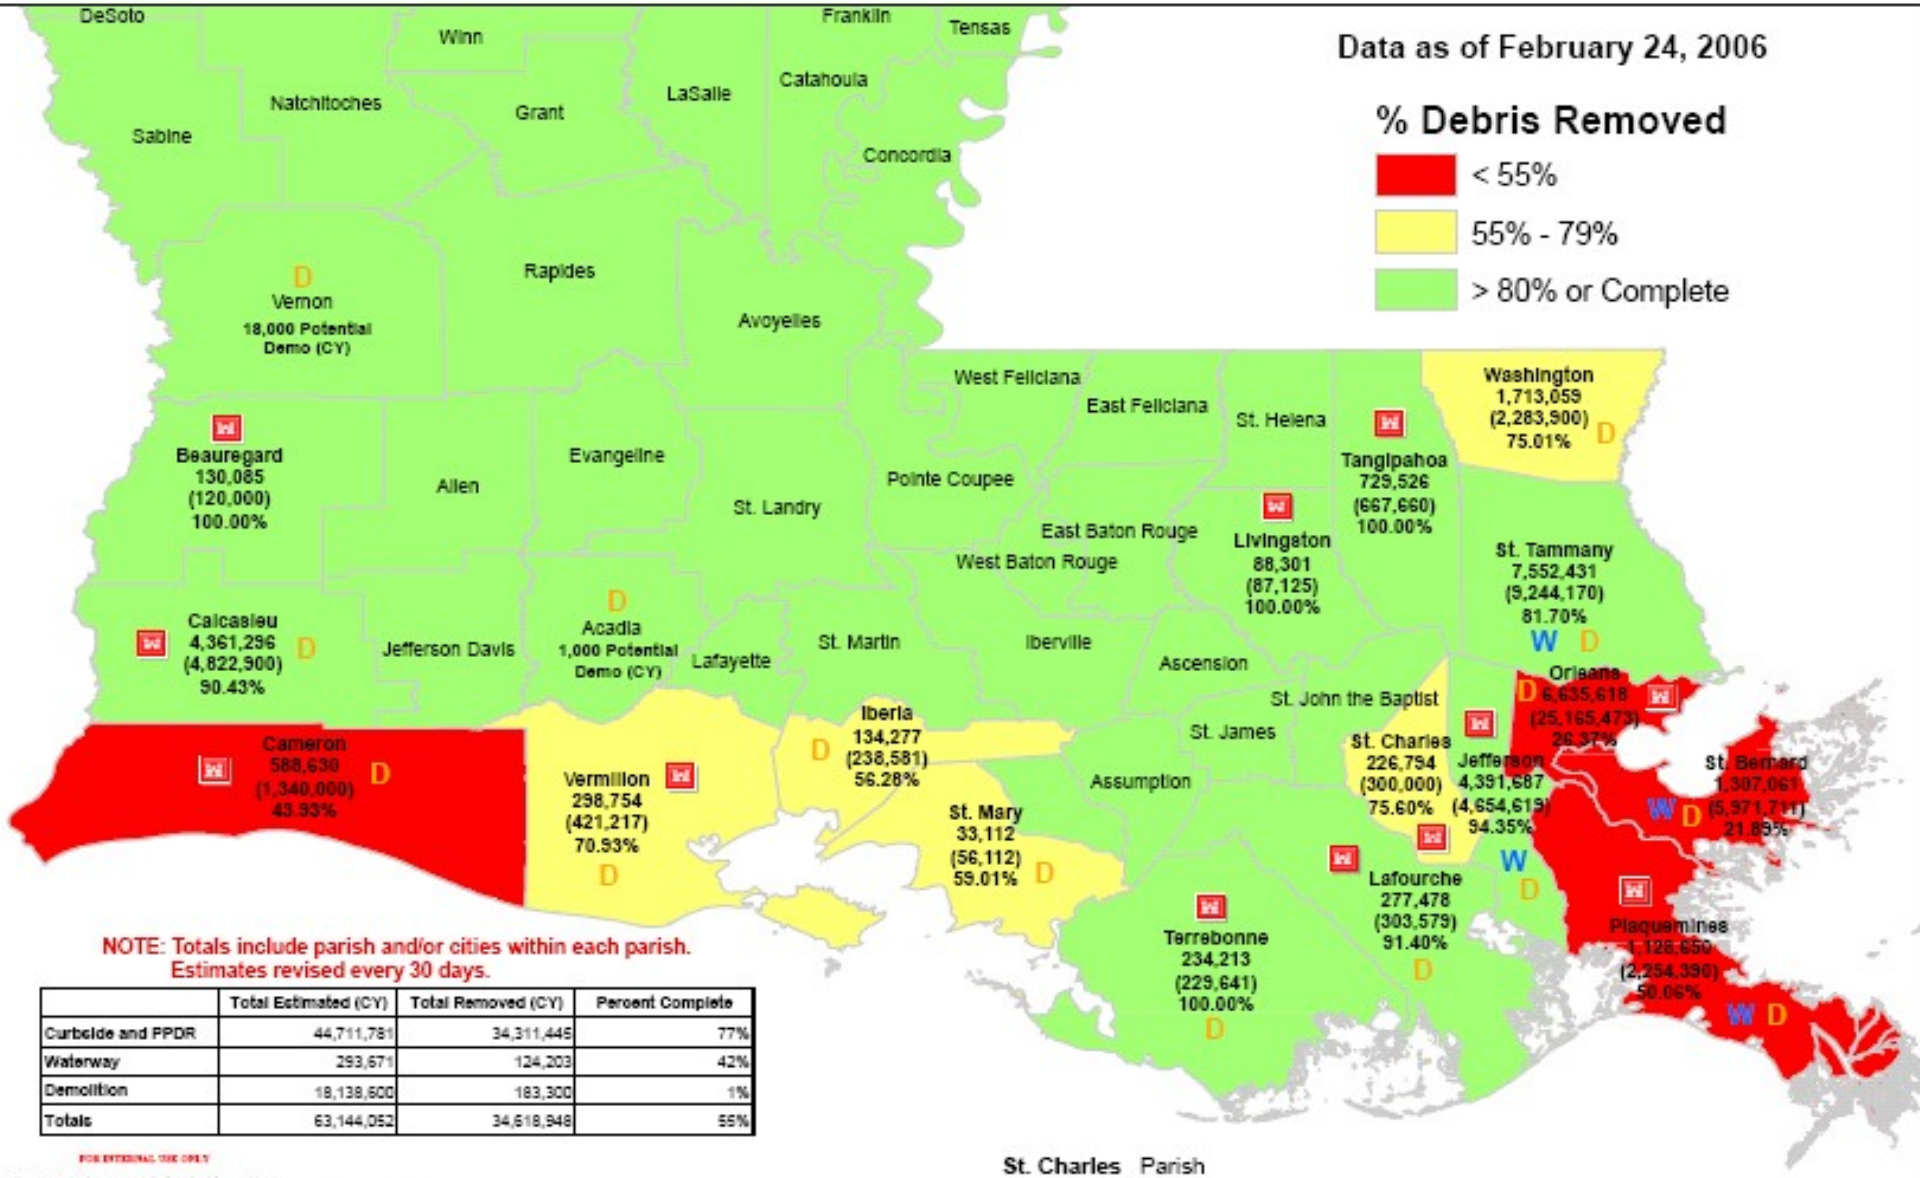

NOTE: Totals include parish and/or cities within each parish.
Estimates revised every 30 days.

	Total Estimated (CY)	Total Removed (CY)	Percent Complete
Curbside and PPDR	44,711,781	34,311,445	77%
Waterway	293,671	124,203	42%
Demolition	18,138,600	183,300	1%
Totals	63,144,052	34,618,948	55%

FOR INTERNAL USE ONLY

Note: Road data layers are periodically updated for completeness and accuracy which may not be reflected on this map.

This product may be protected by one or more copyrights and license restrictions. Neither this document nor the material contained therein may be reproduced, stored in a retrieval system or transmitted in any form or by any means without the prior permission of FEMA.

Geospatial Intelligence Unit, JFO
Version: 20060224 1220
CA_Debris_Status_20060222_MAP_USA_Eval

Active Parishes Managed by USACE
(All other Active Parishes are Applicant Managed)

W Parish Includes Waterway Debris

D Parish/City Includes Demolition Debris

St. Charles Parish

226,794 Total Removed (CY)

(300,000) Total Estimated (CY)

75.60% Percent Complete

US Army Corps of Engineers

Louisiana Temporary Housing

FEMA

- FEMA estimated need: 98,000 units
- 47,632 currently leased
- Mission is ongoing

Travel Trailer Sites
Louisiana, March 6, 2006

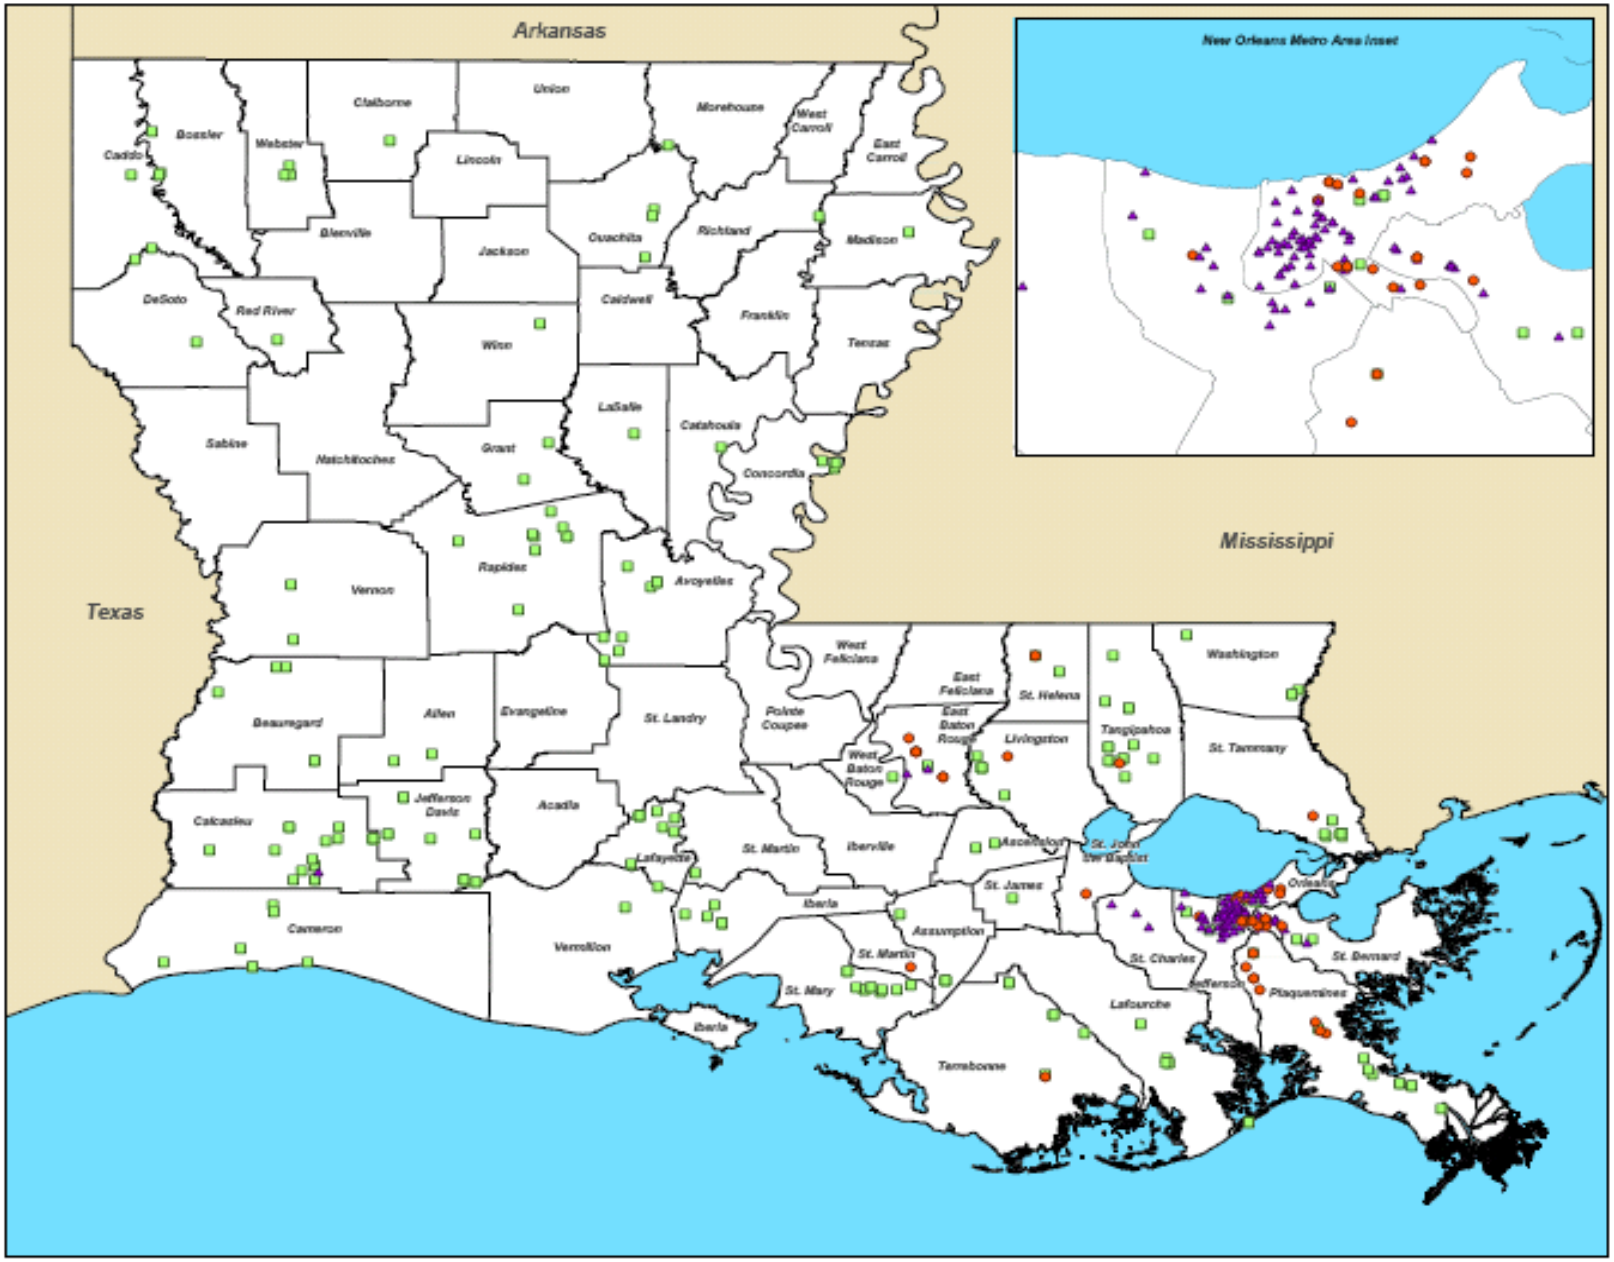

*EG stands for Emergency Group Site

US Army Corps of Engineers

Katrina Timeline for Texas

FEMA

- 08/29: Hurricane Katrina made landfall in southeastern Louisiana as a Category four (4) hurricane; as a result an estimated 427,000 people evacuated to Texas
- 09/02: President declares FEMA-3216-EM-TX
- 09/12: JFO becomes fully operational in TX

US Army Corps of Engineers

Rita Timeline for Texas

FEMA

- 09/19: JFO Designated as RRCC for Hurricane Rita
- 09/20: The RRCC for Hurricane Rita begins operations in the Austin JFO
- 09/21: President declares FEMA-3261-EM-TX
- 09/24: At 0230 CDT Hurricane Rita makes landfall near Sabine Pass, Texas as a Category three (3)
- 09/24: President declares FEMA-1606-DR-TX
- 09/24: Texas JFO opened in Austin; RRCC continues operations

Hurricane Rita - 24 Hour Stage III Rainfall and Wind Speeds

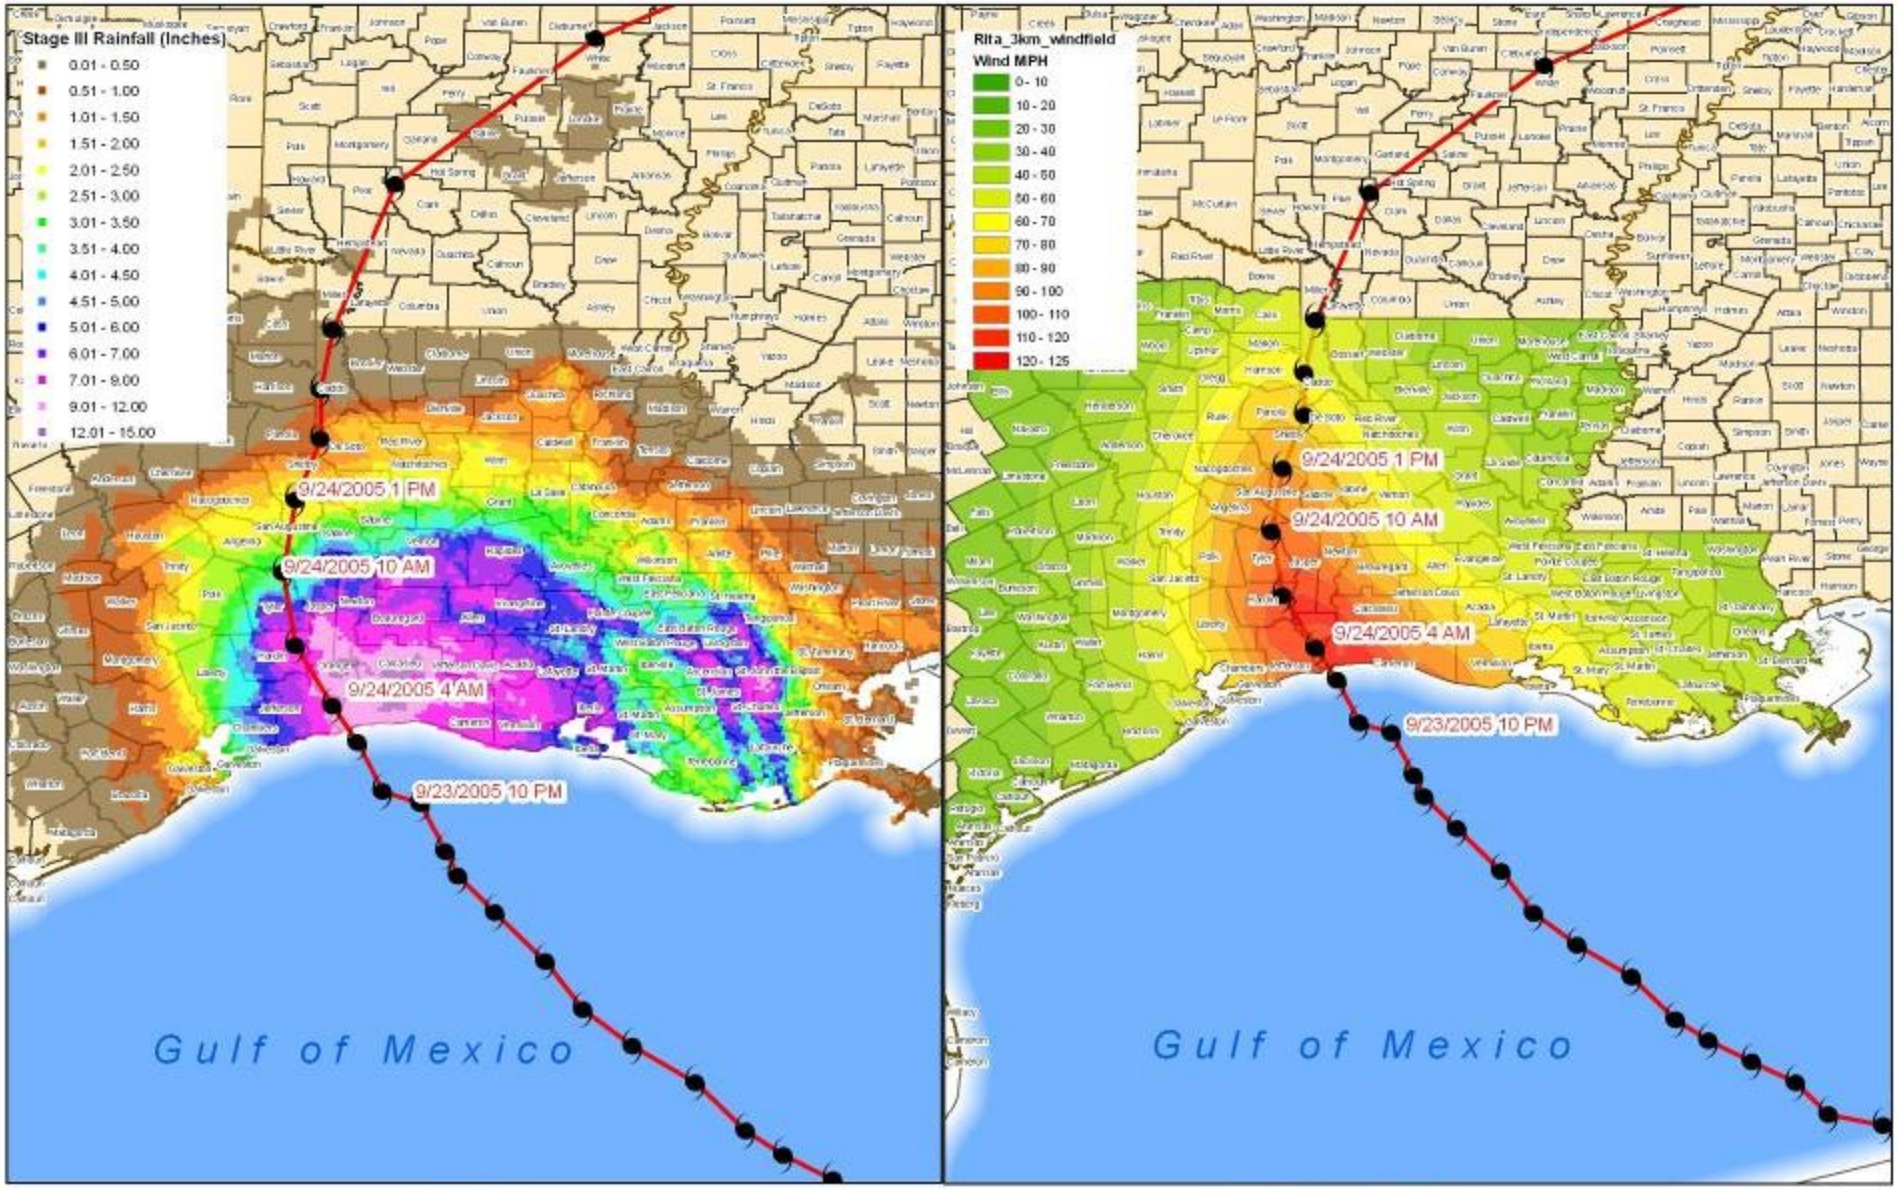

RITA Track

FEMA

ID: FEMA-1606-DR-TX
FEMA-AUSTIN RRCC/JFO; DATE: 12/22/05
Rainfall_Wind_20051222.mxd
GIS: EMAAK

US Army Corps of Engineers

Miles
50 25 0 50 100 150 200

US Army Corps of Engineers

FEMA

Texas Commodities

- Ice
  - 744 Truck loads delivered (3M lbs/$17M)
- Water
  - 909 Truck loads delivered (4.5M gallons/ $16M)
- Power
  - 289 generators installed ($41M)

US Army Corps of Engineers

Temporary Roofing Operation Blue Roof for Texas

FEMA

- 22 Counties
- Over 20,000 installed
- $44M ($2,100/house)

Hurricane Rita - Roofing Mission Status

Roofs Completed: (Total)
Est. 20874

- Angelina County: 50
- Brazoria County: 0
- Chambers County: 139
- Fort Bend County: 0
- Galveston County: 194
- Hardin County: 1471
- Harris County: 7
- Jasper County: 997
- Jefferson County: 11955
- Liberty County: 270
- Montgomery County: 2
- Nacogdoches County: 8
- Newton County: 402
- Orange County 4483
- Polk County: 41
- Sabine County: 64
- San Augustine County: 32
- San Jacinto County: 2
- Shelby County: 1
- Trinity County: 3
- Tyler County: 513
- Walker County: 0

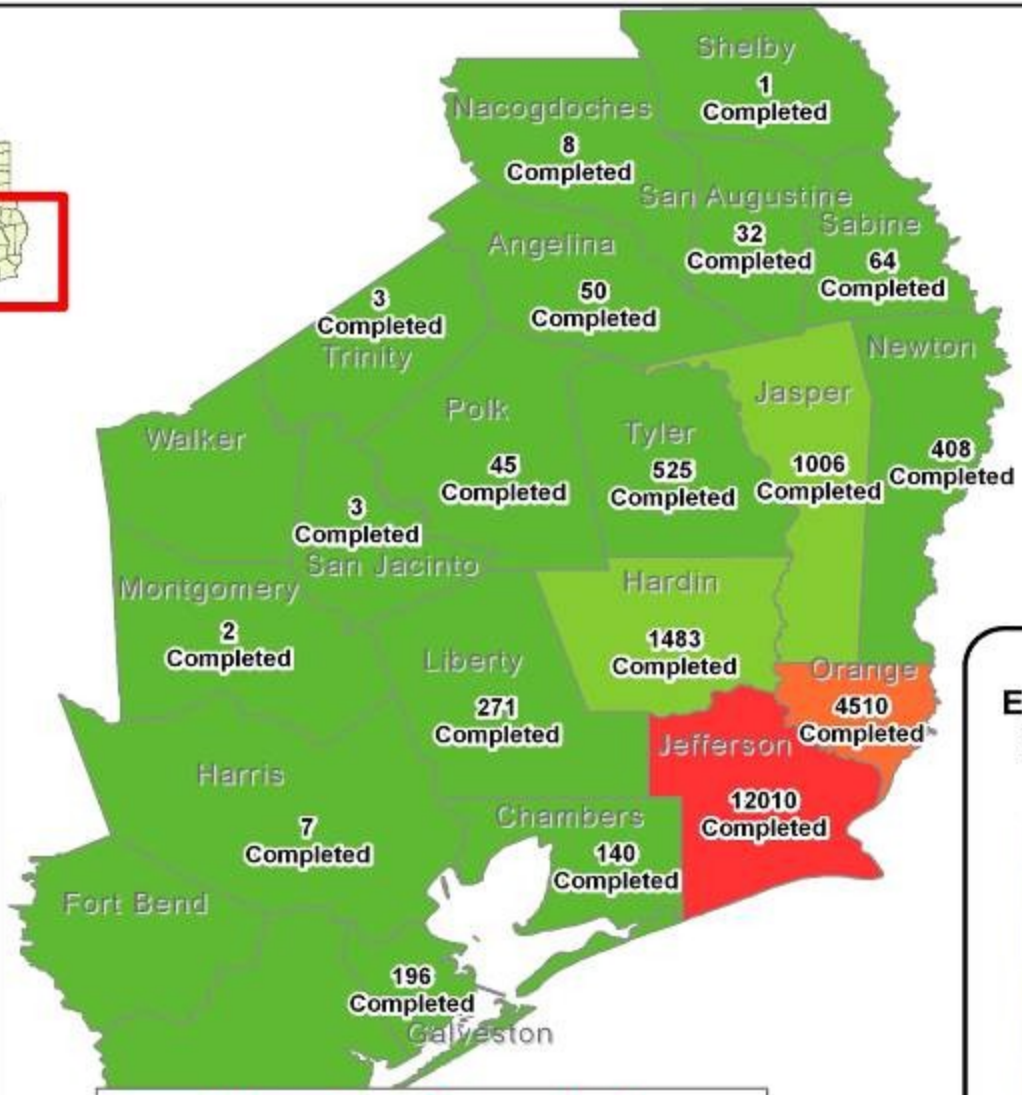

Mission Complete
20,870 Roofs Completed

Estimated Damaged Roofs per County

18 December 2005

- 0 - 1000
- 1001 - 2000
- 2001 - 3000
- 3001 - 4000
- 4001 - 5000
- 5001 - 6000
- 6001 - 7000
- 7001 - 15000

FEMA

ID: FEMA-1609-DR-TX
FEMA-AUSTIN RRCC/JFO; 12/18/05 1200
Roofing_SITREP_20060303.mxd
GIS: E.Mask

US Army Corps of Engineers.

20 10 0 20 40
Miles

US Army Corps of Engineers

Debris Removal for Texas

FEMA

- 8.6 million CY total estimated
- 8.5 million CY removed / 99% complete
- USACE 4.8 million CY / $150 million ($22/CY)
- 19,170 stumps removed
- 13 sunken vessels removed from waterways

Hurricane Rita: Debris Mission Status

Total Quantity Remaining, 58,630
Quantity Removed By County, 3,773,650
Grand Total: 8,613,979 CuYds 99% Complete
Quantity Removed By USACE, 4,840,329

Estimated / Remaining (In CuYds)

Alabama Coushatta: 10790 / 0
Angelina: 198000 / 0
Brazoria: 16351 / 0
Chambers: 45405 / 0
Cherokee: 1000 / 0
Fort Bend: 820 / 0
Galveston: 47897 / 0
Hardin: 1158783 / 39184
Harris: 172455 / 0
Jasper: 554298 / 9645
Jefferson: 2697881 / 9049
Liberty: 114607 / 0
Montgomery: 55000 / 0
Nacogdoches: 57256 / 0
Newton: 350000 / 3714
Orange: 2135000 / 22579
Polk: 34360 / 0
Sabine: 91000 / 1815
San Augustine: 25000 / 0
San Jacinto: 15244 / 0
Shelby: 500 / 0
Trinity: 1900 / 0
TX DOT: 100000 / 100000
Tyler: 832000 / 1901
Walker: 31000 / 0

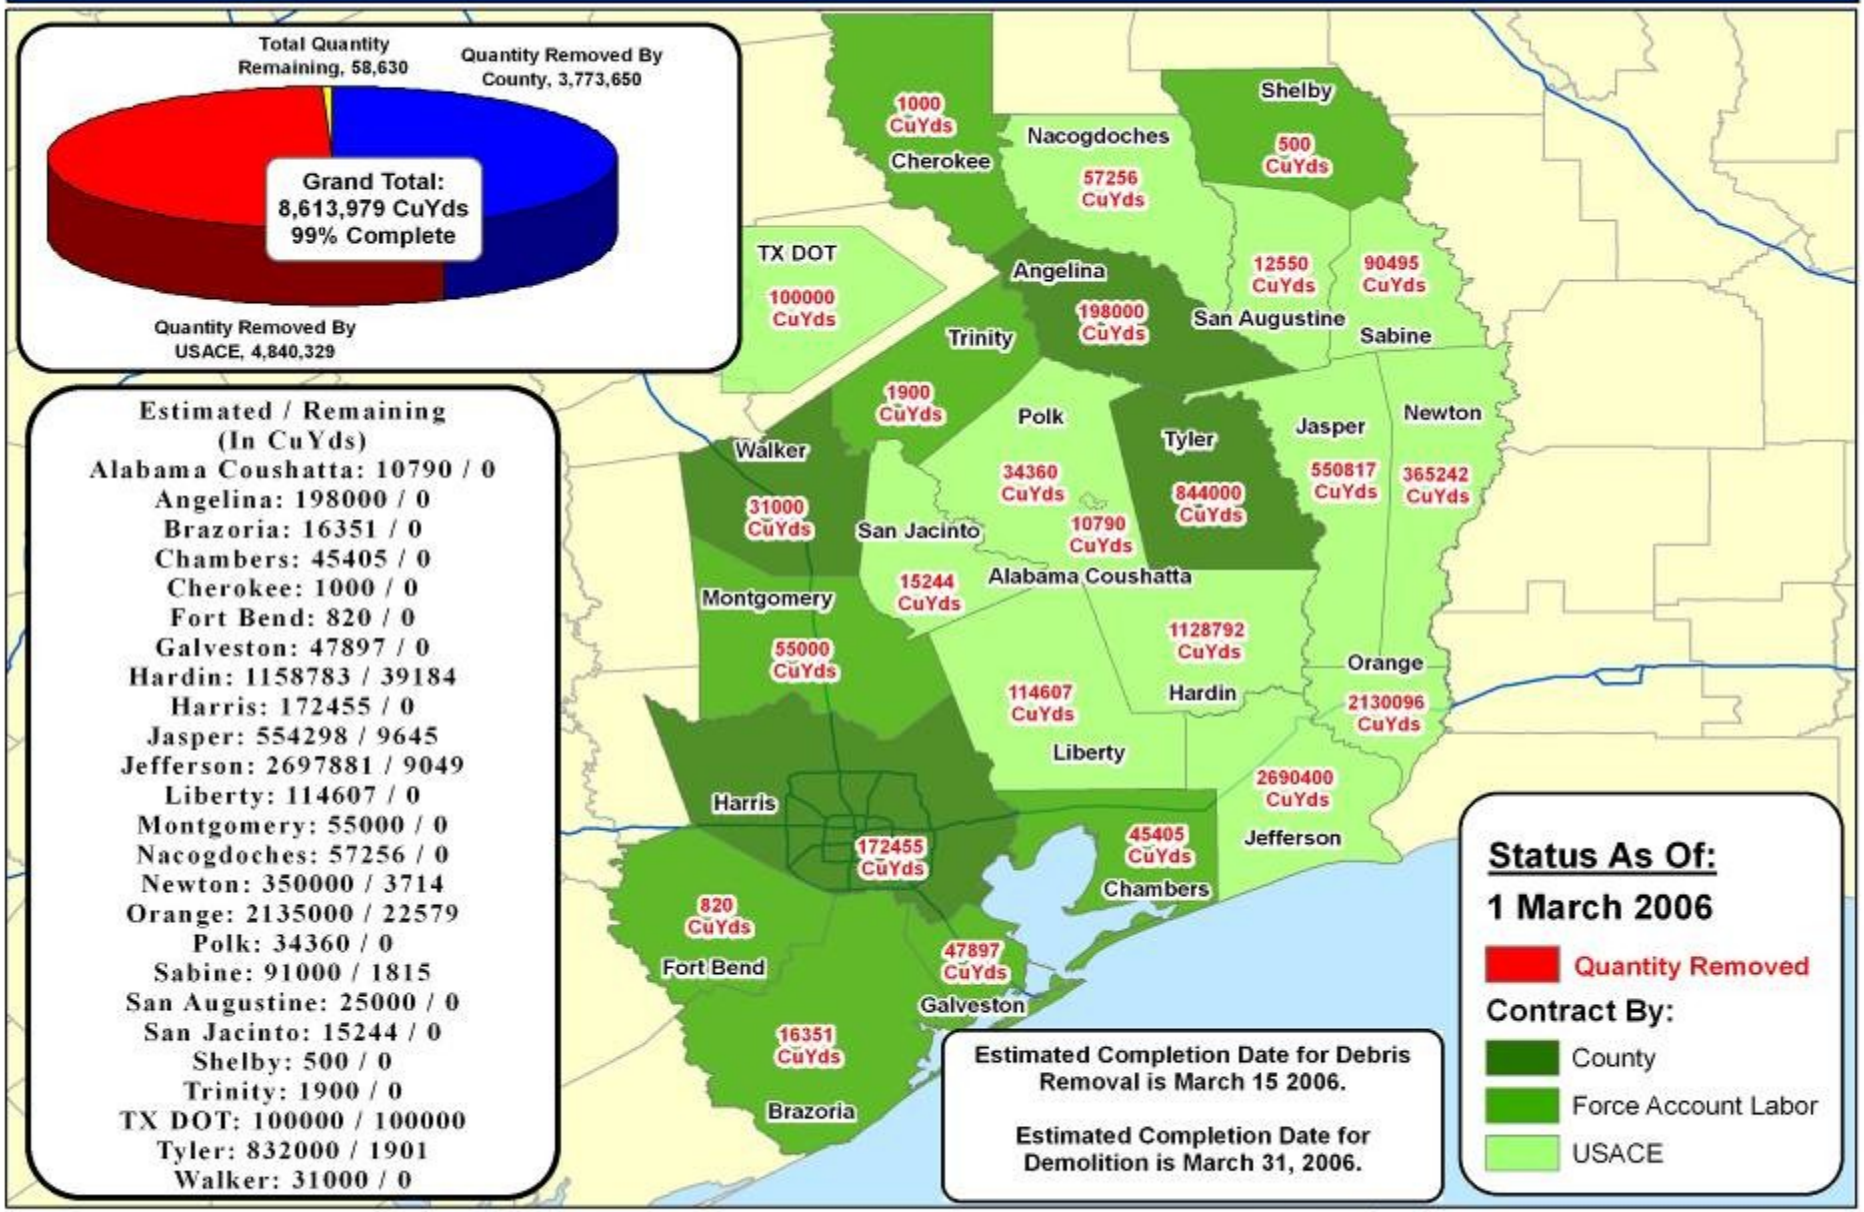

FEMA
ID: FEMA-1606-DR-TX
FEMA-AUSTIN RRCC/JFO; 3/01/06
Debris_Removal_USACE_20060303A.mxd
GIS: EMAAK
US Army Corps of Engineers.

Miles
10 5 0 10 20 30 40 50 60

Hurricane Rita - Sunken Vessel Removal

Total Grounded/Sunken Vessels in TX & LA:	111
Recovered (Cases Closed):	58
Remaining (Open Cases):	53
Active Removal:	0
Cases under ESF-3:	34
Cases under ESF-10:	29
Cases Located in Louisana:	17

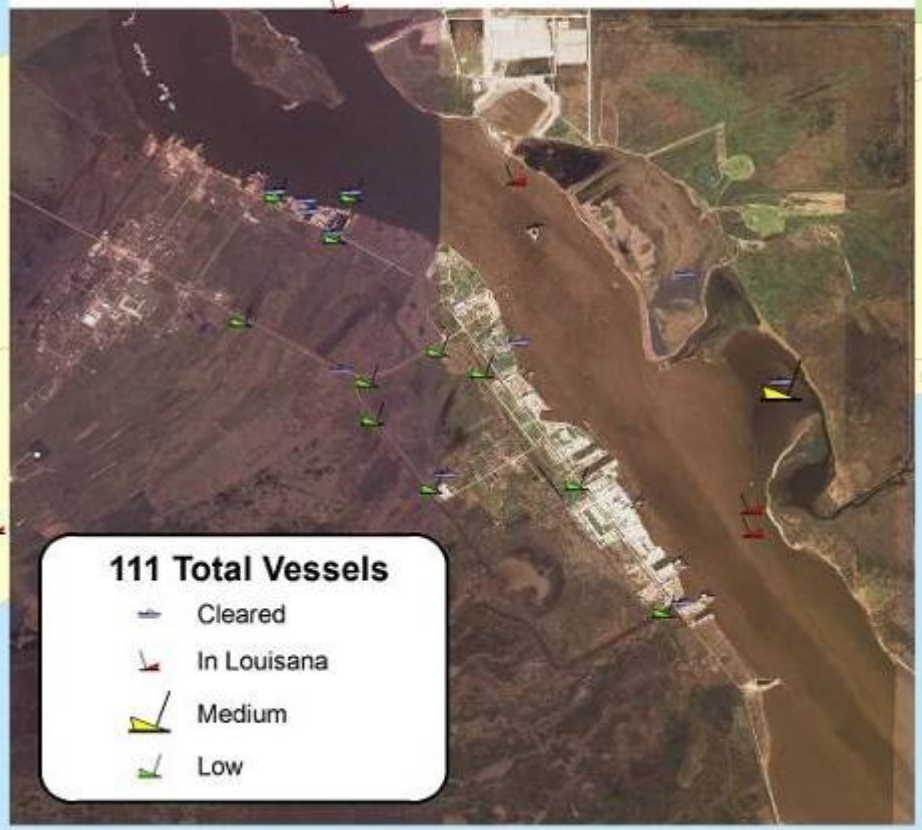

U.S. Department of Homeland Security
United States Coast Guard

FEMA

ID: FEMA-1606-DR-TX
FEMA-AUSTIN RRCC/JFO; 12/03/05; 2130
Vessels_USCG20051203.mxd
GIS: E Maak

2.5 1.25 0 2.5
Miles

US Army Corps of Engineers

Texas Temporary Housing

FEMA

- FEMA estimated need: 3,900 - 4,200 units
- 3,612 currently leased
- $150 million ($50K/set)
- Mission is ongoing

Travel Trailers Leased as of 25 February 2006

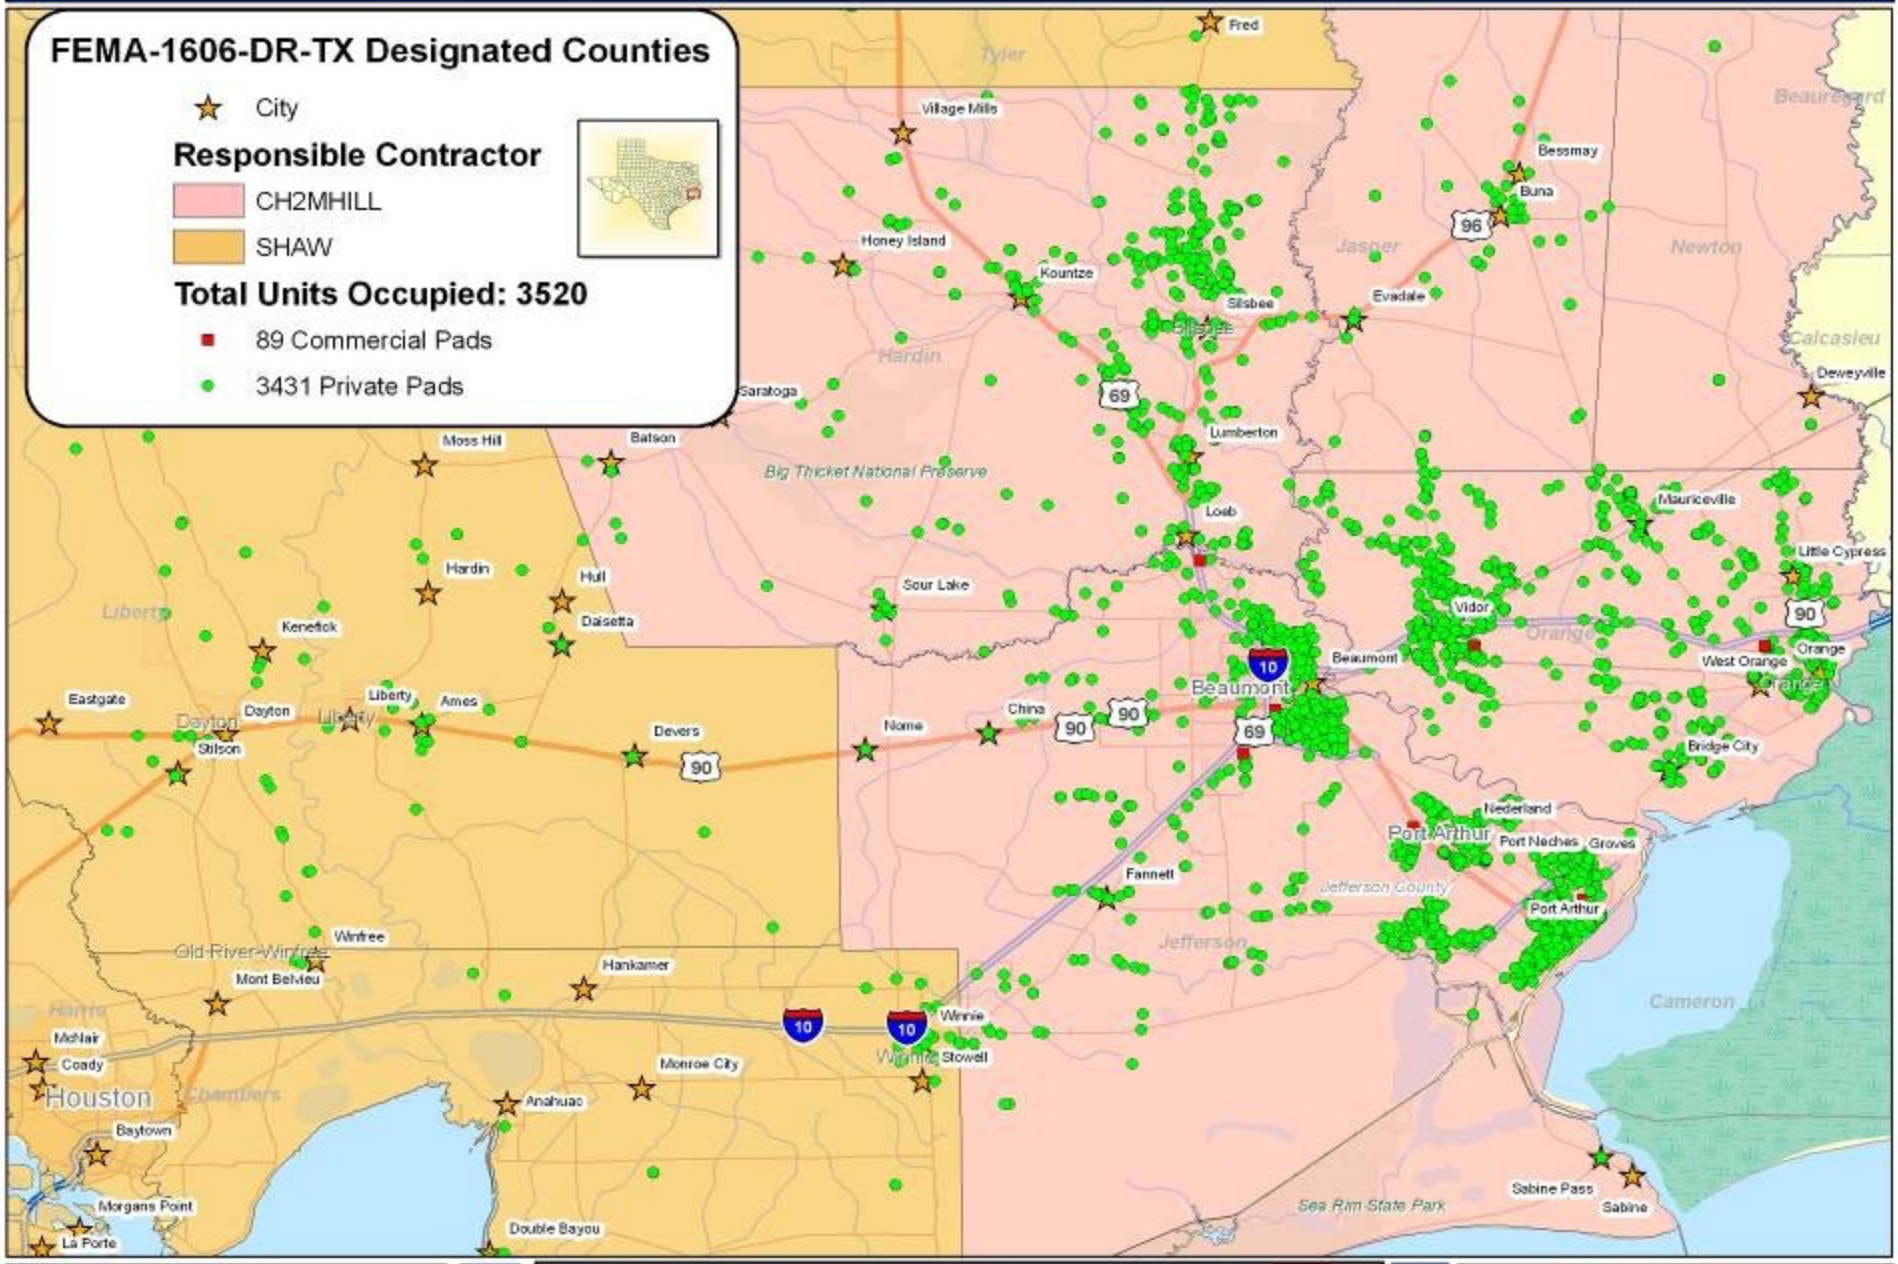

FEMA

ID: FEMA-1606-DR-TX
FEMA-AUSTIN RRCC/JFO; 02/27/06
TT_DHOPS_BRIEF_20060225.mxd
GIS: EMAAK, EDUDLEY

US Army Corps of Engineers

Miles
0 2.5 5 10 15 20

US Army Corps of Engineers

FEMA

Lessons Learned

- Need for more USACE personnel in response (RRCC) to multiple missions (levies, water, ice, generators)
- USACE contract language definitions:
  - “installed” vs. “operating” generators created confusion
  - “installed” vs. “inspected” roofing created confusion

US Army Corps of Engineers

FEMA

Best Practices

- During the Disaster:
  - Planning and Response Team (PRT) leaders from USACE were co-located with RRCC
  - RRCC was co-located with the JFO so operations transitioned smoothly from RRCC response to JFO response and recovery
  - USACE representative embedded in Planning (GIS)
    - Invaluable for response and recovery
    - Facilitated easier communication
    - Common operational picture regarding USACE operations
